M/s. Maa Santoshi Construction & Erectors

GOVT. APPROVED ELECTRICAL CONTRACTORS

Specialist in : H.T. & L.T. Line Construction, Industrial Wiring, Repair & Maintenance of Electrical Equipments, Fabrication & Erection of Lighting Tower.

Ref. No. ..... *Date* .....

To

The Managing Director,
Odisha Knowledge Corporation Ltd.,
Bhubaneswar.

Subject: Verification report of ICT lab

Dear Sir,

We are a registered contractor with Name as M/S. Maa Santoshi construction & Erectors, an approved Electrical contractor of Government of Odisha, bearing Licence No. 1926 (HT) (Copy of license is enclosed) for your kind perusal.

After verification of the following items of the ICT lab at GOVT. (SSD) HIGH SCHOOL, Khedapada UDice Code: 21270712802, Block/NAC/Municipality Kolnara, District Rayagada as per the minimum specification mentioned below, the report for the same is being attached.

Sr. No.	*Item name*	*Minimum Specifications*	*Quantity*
1	Earthing (as per IS specifications)	Copper plate earthing stations making earthing with copper earth plate	1
		600 mm x 600 mm x 3 mm thick including funnel, charcoal/coke, salt, all earth work.	
2	Switches and sockets (ISI Mark)	5 A- 240 V switches	15
		2 in 1 5A and 15A Sockets	15
		15 A – 240 V socket with shutter	2

AT : BIKASH NAGAR, P.O. : P.T.C., DIST. : ANGUL (ODISHA), PH. : 06764 - 230525, M. : 9438235777

		Indicative Brands: - Anchor / Havells / crabtree /Wipro /Phillips / Legrand (Pls. tick) Switches and sockets is to be provided for all electronics/IT equipment including printer and Projection System to be placed at lab technician table.	
3	Wiring (ISI Mark)	PVC conduits including MS/GI boxes. All wires should be covered, insulated and properly clamped. Wiring for 5 and 15A power outlets with 4 square mm PVC insulated stranded copper conductor wires Earthing of 3rd pin with PVC insulated green color 2.5 square mm copper wire	Full Lab

Findings:

1. Earthing (as per IS specifications) : **All OK** **2 Ohms**
2. Switches and sockets (ISI Mark) :

	Status	Qty.	Brand
5 A- 240 V switches :	**OK**	**23**	**Anchor**
2 in 1 5A and 15A Sockets:	**OK**	**19**	**Anchor**
15 A – 240 V socket without shutter:	**OK**	**01**	**Anchor**

3. Wiring (ISI Mark)
   PVC conduits including MS/GI boxes. **All OK**
   All wires covered, insulated and properly Clamped.
   Wiring for 5 and 15A power outlets: with **2.5 square mm** PVC insulated trended copper conductor wires
   Earthing of 3rd pin: with PVC insulated green colour **1.5 square mm copper wire**

With regards

Name & Signature with seal

M/s Maa Santoshi
Construction & Erectors
Electrical Contractor

Encl.

1. Verification report for the given items
2. Electrical contractor's licence copy

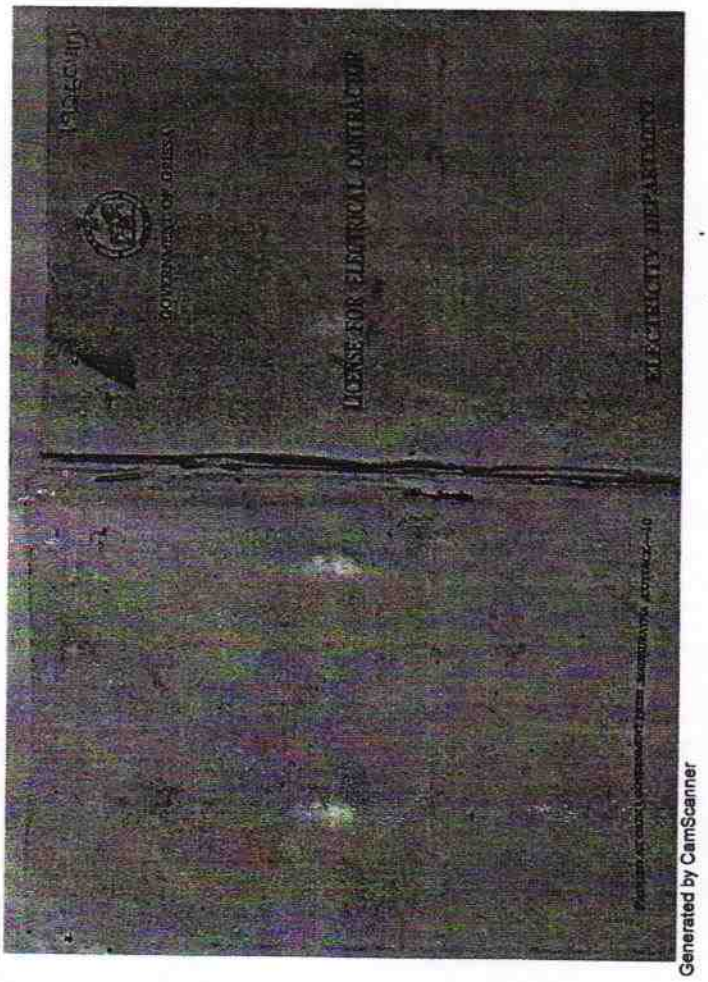

Generated by CamScanner

FORM 'D'

(Regulation 28)

ELECTRICAL CONTRACTOR'S LICENSE

This liconse is to be renewed for a period of three years at a time and must be produced on demand by the Secretary.

(Not transfemble or renewable by any authority other than the Electrical Licensing Board of Orissa).

I do hereby certify that Messers/Shri. M/s Maa Santoshi Control & Erectors have this day been granted license to carry out electrical installation work of the following class/classes in the State of Orissa for the purpose of rule 45 (I) of Indian Electricity Rules 1956.

Name and address of the person/firm to whom license is issued.	M/s Maa Santoshi Control & Erectors Prop. Krishan Chandra Agarwal At. Bidyadhar Nagar P.O. PTC Dist. Angul.
Date of approval by Electrical Licensig Board, Orissa	To be Renewed.
Date of issue of license	27.12.2008
Type of electrical installation work for which license is issued.	Allowed to execute Electrical Installations for HT Works upto 11KV Cable Jointing.
Registration No.	1926 (HT)

27/12/08
Electrical Inspector to the Government of Orissa and Secretary, Electrical Licensing Board

Generated by CamScanner

Date of renewal	Date of expiry	Signature of Electrical Inspector and Secretary, Electrical Licensing Board, Orissa
1	2	3
PROVISIONALLY ALLOWED PER 1 YEAR i.e. FROM 26.12.2008 TO 25.12.2009. SUBJECT TO RATIFICATION BY ELBO. 27/12/08 SECRETARY ELBOA		
01. B. Pal Secty upto 02. B. Banik Upto 580 KMP 03. S. Khanra Upto 580 AGL 04. N.C. Saha Upto 1676 AGL 05. S.K. Bhanja Upto 1684 AGL 06. I. Kar Upto 212 AGL DN:- 5MVA, 11 KV, 1000V, 0.2 mA/m ET:- 15529, CSE, 0.100 Ω		SECRETARY ELBOA 29/12/09

Ratified in 127th Meeting of ELBO held on 29.4.2009.

26.12.2009	25.12.2012	SECRETARY ELBOA 5/1/10
Present Status		
1. B Pal Secy CHD No-4847	03.08.2014.	
2. B. Banik U/M Upto-KMP-580	11.8.2015	
3. S. Khanra U/M Upto AGL-580	27.3.2015	
4. N.C Saha U/M Upto AGL-1676	12.5.2018	
5. S.K Bhanja U/M Upto AGL-1684	12.5.2018	SECRETARY 2/1/13
6. I. Kar U/M Upto AGL-212	27.8.2016	SECRETARY ELBOA 22/1/13

Generated by CamScanner

Date of renewal	Date of expiry	Signature of Electrical Inspector and Secretary, Electrical Licensing Board, orissa
1	2	3
6.12.2012	25.12.2015	SECRETARY ELBO Dist

N.B.-This License will become Invalid if Permit/Certificate of any of the above staff becomes invalid.

SECY ELBO Dist

Generated by CamScanner
